




		Name	Duration	Start	Finish
1		☐ Design, Manufacture and Commission of Nodes	427 days?	24/02/25 8:00 AM	16/07/25 4:00 PM
2		☐ CEN	271.125 da...	24/02/25 8:00 AM	25/05/25 5:00 PM
3		☐ MOTHER Board V2	271.125 da...	24/02/25 8:00 AM	25/05/25 5:00 PM
4		Design	148.125 days?	24/02/25 8:00 AM	14/04/25 5:00 PM
5		Shipping	43.125 days?	14/04/25 5:00 PM	29/04/25 2:00 AM
6		Manufacture and Commission	79.875 days?	29/04/25 2:00 AM	25/05/25 5:00 PM
7		☐ BSPD V3	64 days?	26/02/25 8:00 AM	19/03/25 4:00 PM
8		Design	30 days?	26/02/25 8:00 AM	8/03/25 8:00 AM
9		Shipping	14 days?	12/03/25 8:00 AM	17/03/25 12:00 AM
10		Manufacture and Commission	8 days?	17/03/25 12:00 AM	19/03/25 4:00 PM
11		☐ Pedal Box Redesign	331.125 da...	24/02/25 8:00 AM	14/06/25 5:00 PM
12		Pedal Box Redesigned	11 days?	24/02/25 8:00 AM	10/03/25 5:00 PM
13		☐ PENV1.2	97.125 day...	13/05/25 8:00 AM	14/06/25 5:00 PM
14		Design	28.125 days?	13/05/25 8:00 AM	22/05/25 5:00 PM
15		Shipping	24 days?	22/05/25 5:00 PM	30/05/25 5:00 PM
16		Manufacture and Commission	45 days?	30/05/25 5:00 PM	14/06/25 5:00 PM
17		☐ HIP	116 days?	24/02/25 8:00 AM	4/04/25 12:00 AM
18		☐ HIPV1.3 PCB	116 days?	24/02/25 8:00 AM	4/04/25 12:00 AM
19		Design	32 days?	24/02/25 8:00 AM	7/03/25 12:00 AM
20		Shipping	14 days?	19/03/25 8:00 AM	24/03/25 12:00 AM
21		Manufacture and Commission	33 days?	24/03/25 12:00 AM	4/04/25 12:00 AM
22		☐ TSAL_Discharge V3	89 days?	24/02/25 8:00 AM	26/03/25 12:00 AM
23		Design	32 days	24/02/25 8:00 AM	7/03/25 12:00 AM
24		Shipping	14 days?	19/03/25 8:00 AM	24/03/25 12:00 AM
25		Manufacture and Commission	6 days?	24/03/25 12:00 AM	26/03/25 12:00 AM
26		☐ AIL V2.1	73.75 days?	27/02/25 8:00 AM	23/03/25 10:00 PM
27		Design	11 days?	27/02/25 8:00 AM	3/03/25 12:00 AM
28		Shipping	14 days?	13/03/25 8:00 AM	18/03/25 12:00 AM
29		Manufacture and Commission	6 days?	18/03/25 12:00 AM	20/03/25 12:00 AM
30		time till LVD arrives	11.75 days?	20/03/25 12:00 AM	23/03/25 10:00 PM
31		☐ LVD V3.2	68 days?	3/03/25 8:00 AM	26/03/25 12:00 AM
32		Design	18 days?	3/03/25 8:00 AM	9/03/25 8:00 AM
33		Shipping	14 days?	19/03/25 8:00 AM	24/03/25 12:00 AM
34		Manufacture and Commission	6 days?	24/03/25 12:00 AM	26/03/25 12:00 AM
35		☐ EXPANSION Board	307.125 da...	3/03/25 8:00 AM	13/06/25 5:00 PM

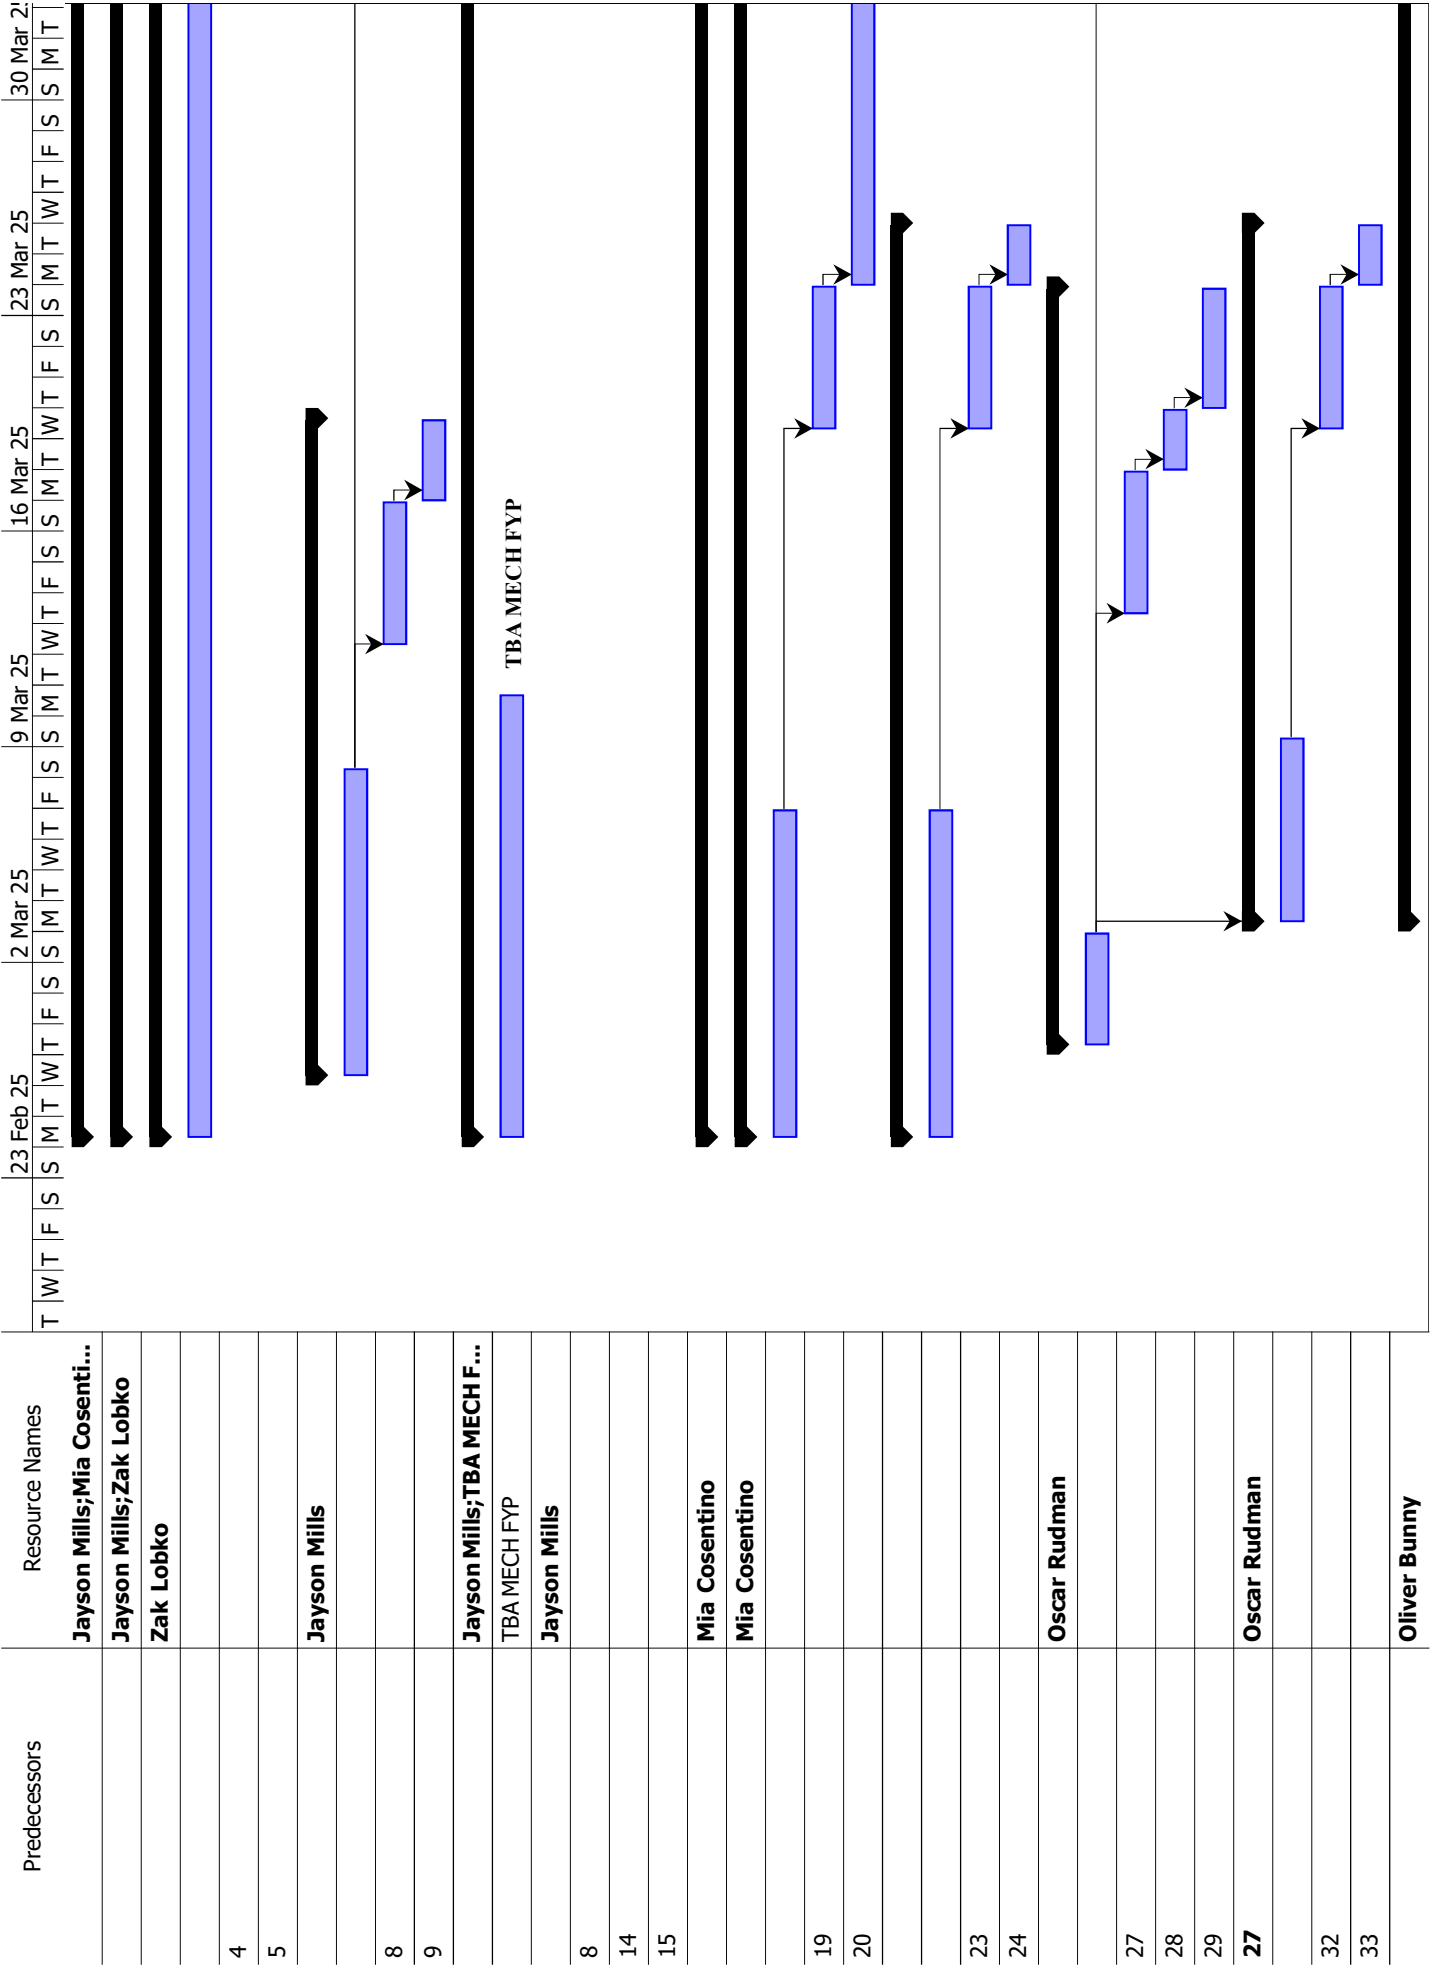

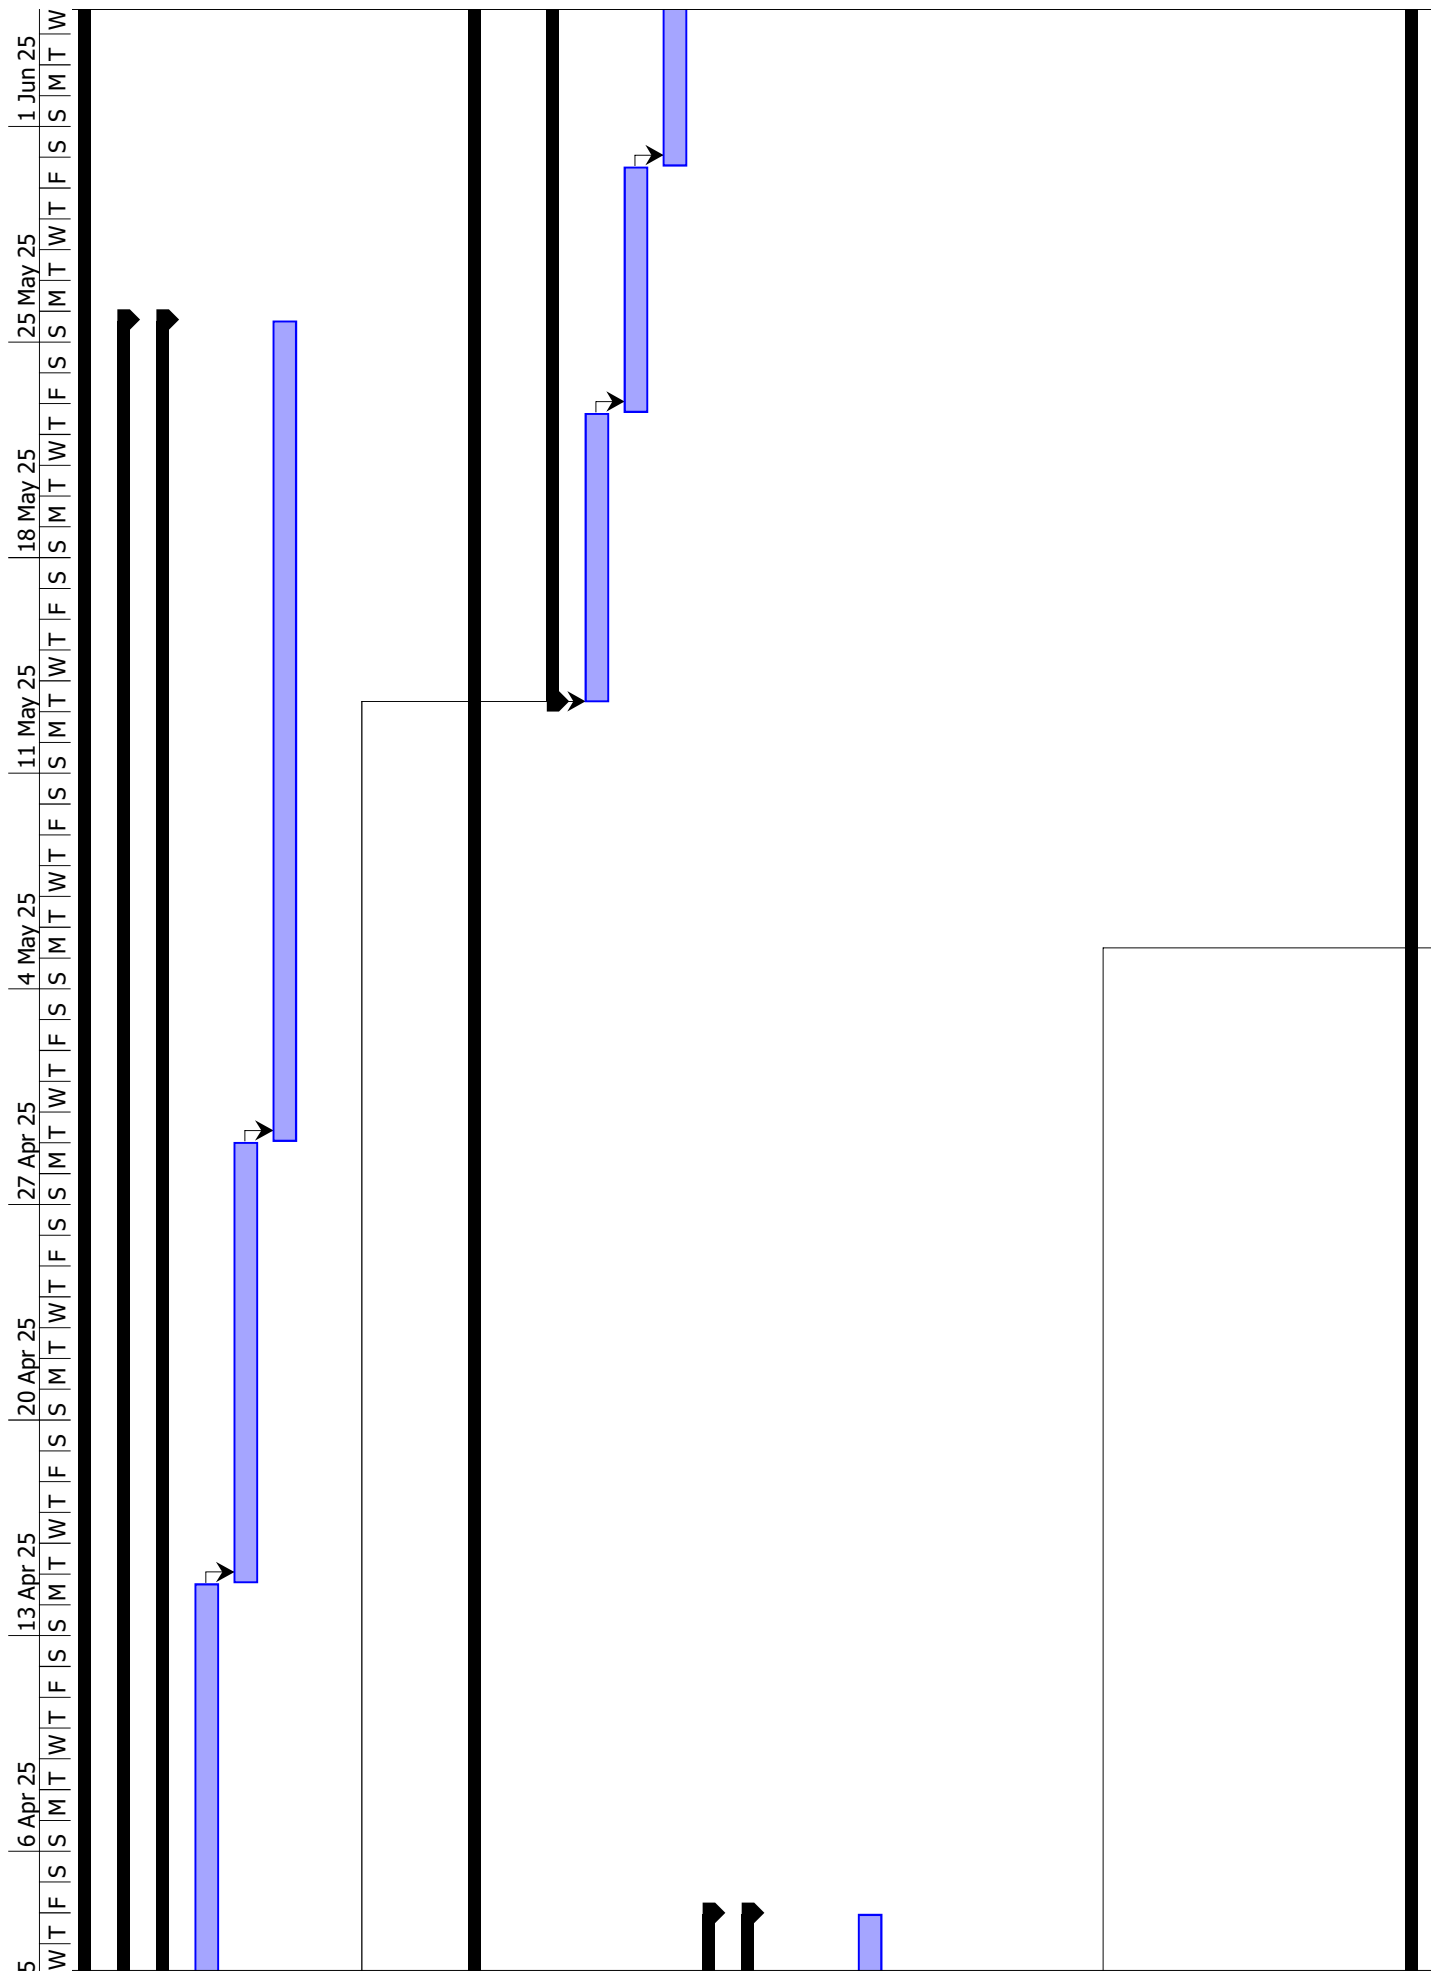

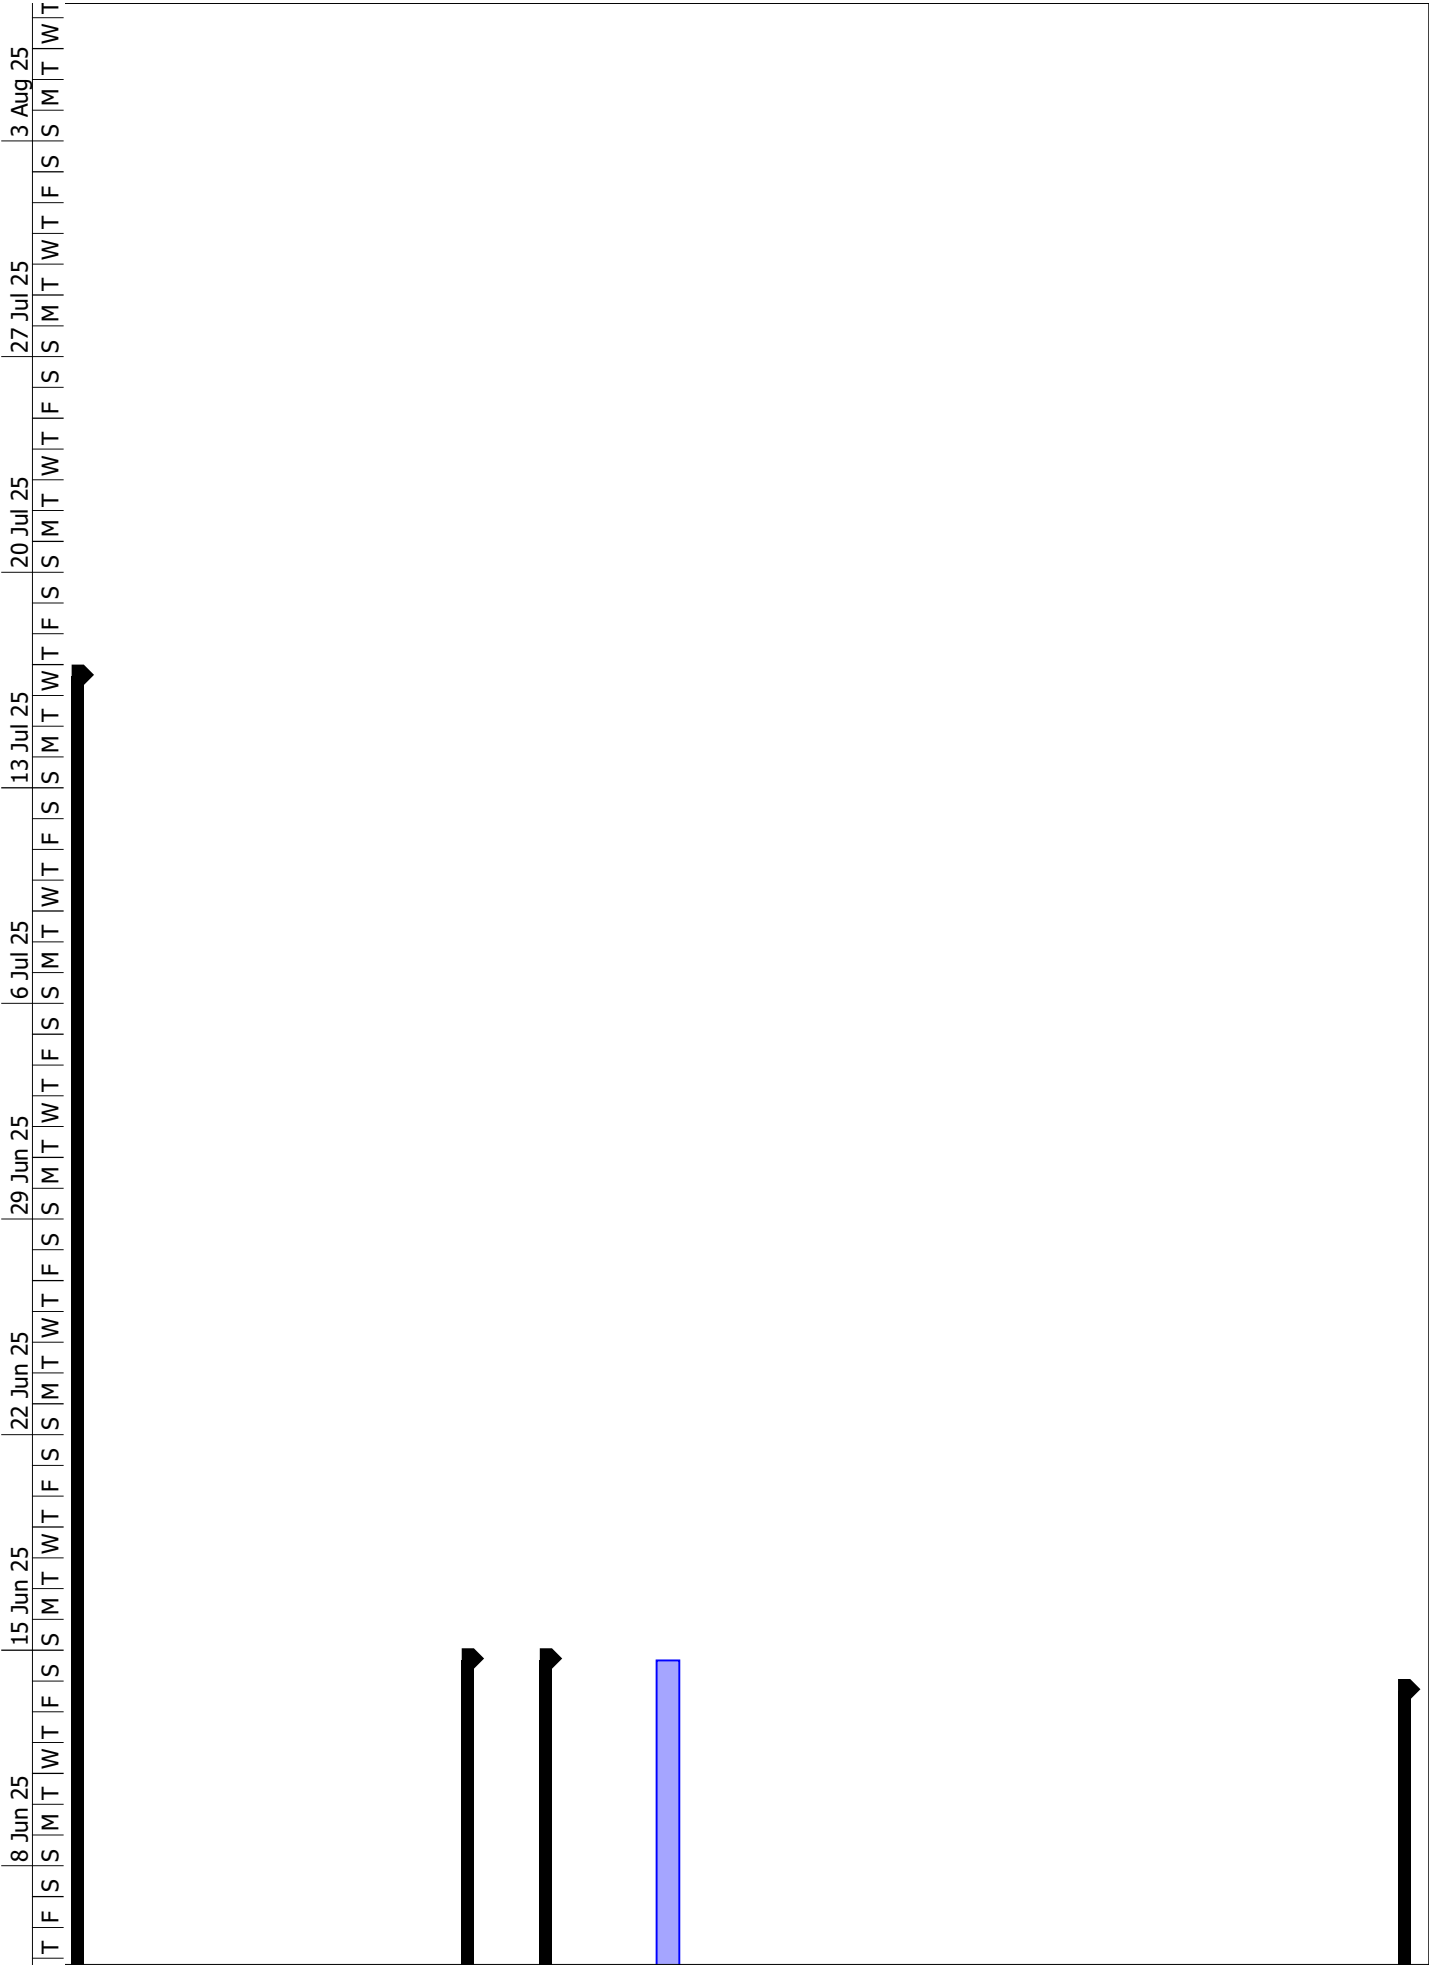



10 Aug 25

· F S M T W T F

		Name	Duration	Start	Finish
36		Design	241.125 days?	3/03/25 8:00 AM	22/05/25 5:00 PM
37		Shipping	25.125 days?	22/05/25 5:00 PM	31/05/25 2:00 AM
38		ManufactureandCommission	13.875 days?	9/06/25 2:00 AM	13/06/25 5:00 PM
39		Wheel turtle test with CANGate	0 days	14/06/25 8:00 AM	14/06/25 8:00 AM
40		Brake Temp sensor test	0 days	26/06/25 8:00 AM	26/06/25 8:00 AM
41		Wheel speed sensor test?	1 day?	16/07/25 8:00 AM	16/07/25 4:00 PM
42		LVD V3.3	112.125 da...	5/05/25 8:00 AM	11/06/25 5:00 PM
43		Design	18 days?	5/05/25 8:00 AM	11/05/25 8:00 AM
44		Shipping	25.125 days?	22/05/25 8:00 AM	30/05/25 5:00 PM
45		Manufacture	3 days?	10/06/25 5:00 PM	11/06/25 5:00 PM
46		NU24 CEN Integration Test	0 days?	24/05/25 8:00 AM	24/05/25 8:00 AM
47		Fault Finding and Fixing	21 days?	24/05/25 8:00 AM	31/05/25 8:00 AM
48		NU24 LVD & HIP Integration Test	0 days	14/06/25 8:00 AM	14/06/25 8:00 AM
49		Potential Test: NU24 PEN & Expansion Board Integration Test	0 days	21/06/25 8:00 AM	21/06/25 8:00 AM
50		NU24 final drive	0 days	30/06/25 8:00 AM	30/06/25 8:00 AM
51		NU25 first drive (with old power box)	0 days	16/07/25 8:00 AM	16/07/25 8:00 AM
52		New uprights (on NU24), test brake temp sensors	0 days	26/06/25 8:00 AM	26/06/25 8:00 AM

Predecessors	Resource Names	23 Feb 25																											
		T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
36																													
38																													
39																													
40																													
27	Oscar Rudman																												
43																													
44																													
46																													
47																													

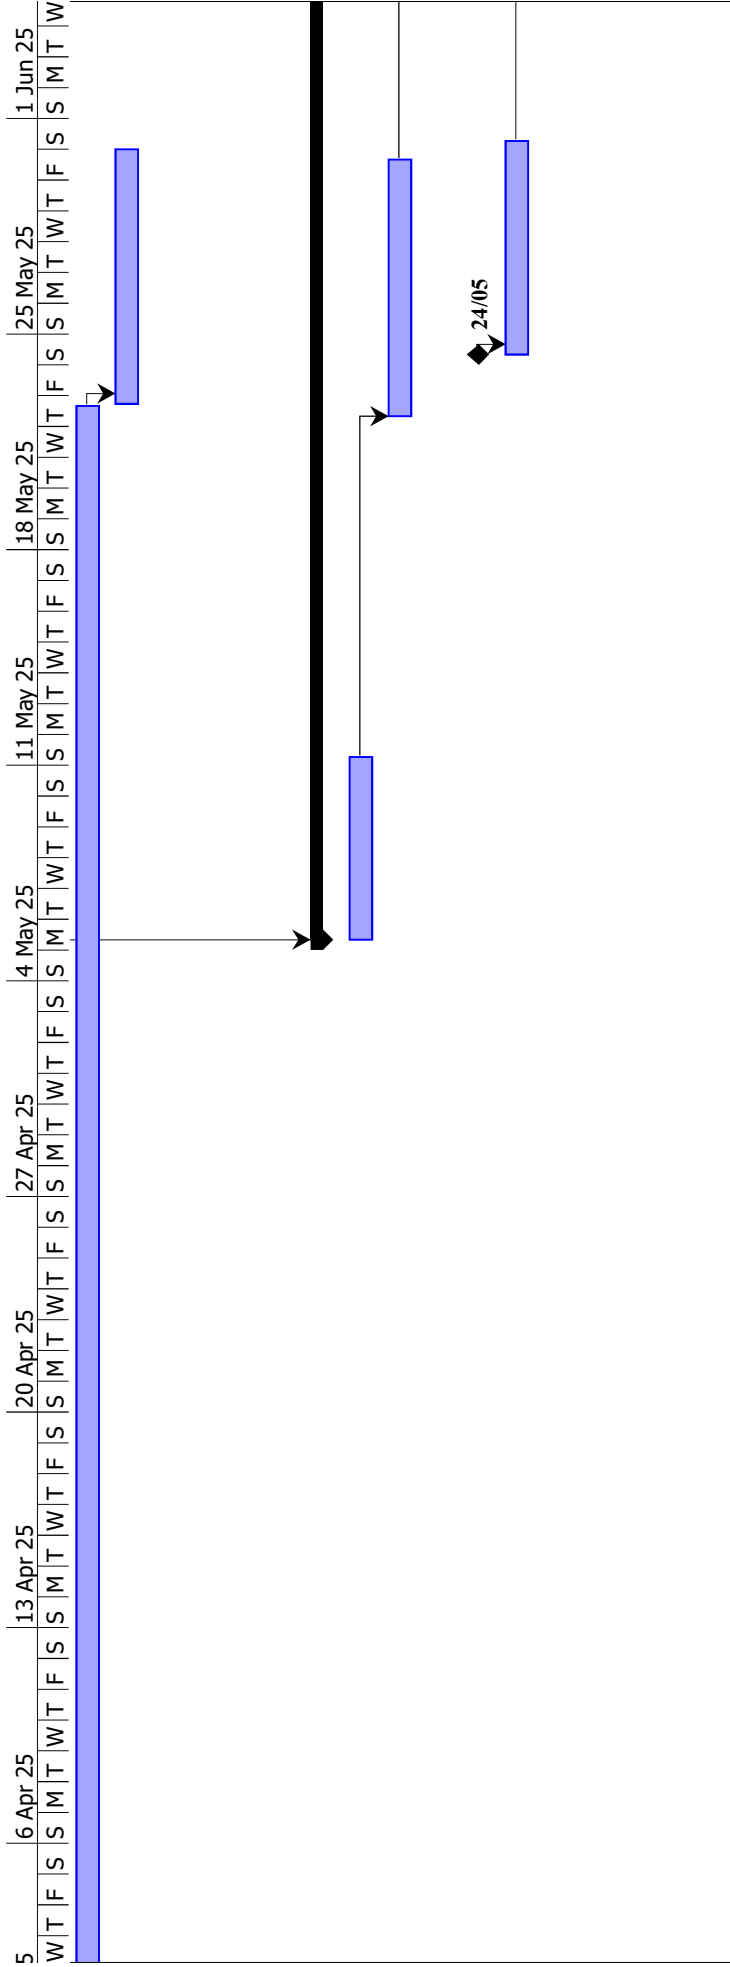

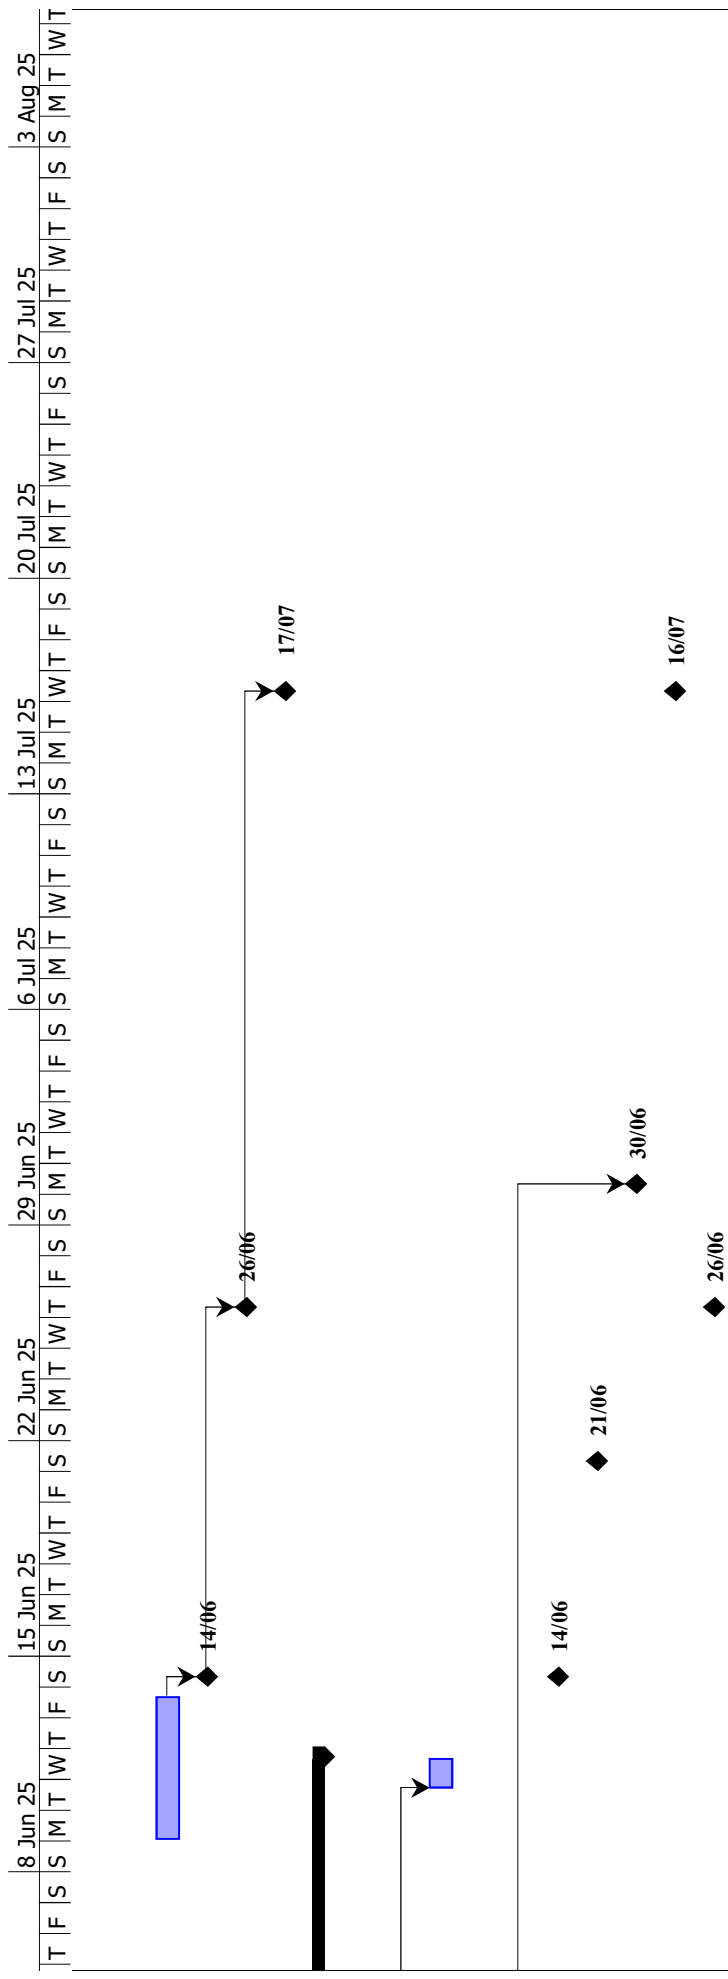

10 Aug 25

.	F	S	S	M	T	W	T	F
---	---	---	---	---	---	---	---	---
